Inspection Report for North Sturbridge Road Solar Facility NPDES ID No.: MAR10031G

NPDES ID No.: MAR10031G Inspection Date: 02/04/2022

			General Inf	ormation				
Weather conditions during inspection	34°F, cloudy, raining		Inspection	9:00AM	Inspection end	9:35 AM		
Inspector Name, Title Contact Information	&	Chanler Florian, Environmental cflorian@beta-inc.com	8603	297045				
Present Phase of Construction		Phase 1. NOTE: The access road and stabilized construction entrance has been established pursuant to the Phase 1 scope of work.  However, the entirety of the Site has been cleared of trees. No grubbing/stumping has occurred other than that required to establish the Site access road.						
		North Sturbridge Road Solar Fac	North Sturbridge Road Solar Facility – Entirety of Site (0 North Sturbridge Road, Charlton, MA 01507)					
Standard Frequency:		may be subject to different inspect	·		, , , , ,			
<ul> <li>☑ Every 14 days and within 24 hours of a 0.25" rain or the occurrence of runoff from snowmelt sufficient to cause a discharge</li> <li>Increased Frequency:</li> <li>☐ Every 7 days and within 24 hours of a 0.25" rain (for areas of sites discharging to sediment or nutrient-impaired waters or to waters designated as Tier 2, Tier 2.5, or Tier 3)</li> <li>Reduced Frequency:</li> <li>☐ Twice during first month, no more than 14 calendar days apart; then once per month after first month; (for stabilized areas)</li> </ul>						rs designated as Tier 2, Tier 2.5,		
<ul> <li>□ Twice during first month, no more than 14 calendar days apart; then once more within 24 hours of a 0.25" rain (for stabilized areas on "linear construction sites")</li> <li>□ Once per month and within 24 hours of a 0.25" rain (for arid, semi-arid, or drought-stricken areas during seasonally dry periods or during drought)</li> <li>□ Once per month (for frozen conditions where earth-disturbing activities are being conducted)</li> </ul>								
Was this inspection triggered by a 0.25" storm event?								

Inspection Report for North Sturbridge Road Solar Facility

NPDES ID No.: MAR10031G Inspection Date: 02/04/2022

Unsafe Conditions for Inspectio
---------------------------------

Did you determine that any portion of your site was unsafe for inspection per CGP Part 4.1.5? 

Yes 
No If "yes", complete the following:

- Describe the conditions that prevented you from conducting the inspection in this location: N/A
- Location where conditions were found: N/A

Condition and Effectiveness of Erosion and Sediment (E&S) Controls (CGP Part 2.2)				
Type/Location of E&S Control	Maintenance Needed?*			
1. Silt Fence and Straw Wattles	Yes (As of 9/2/2021)	No	9/2/ 2021	A breach was observed at Discharge 2. Although the double row of straw bales is intact, silt fence was observed to be knocked over and signs of stormwater flow were detected in the area beyond the fence.  A minor tear was identified in a section of silt fence on the southern side of the Site with no erosion observed.  Minor degradation of a straw wattle was observed on the southeastern side of the Site; no erosion was observed but pools of water were found to be forming behind the straw wattle.
Stabilized Construction Entrance     (Site Entrance – Access Road)	No (As of 9/2/2021)	No		A tree was knocked over and laying on the silt fence on the on the northwestern portion of the site in Zone 5.  Hydroseed was applied to exposed soil in this area and continues to germinate, some grass seedlings are now observed.
<ul><li>3. Stump and Soil Stockpile Area</li><li>4. Dust Controls</li></ul>	No (As of 7/22/2021)	No	10/29/ 2021	Minor tears were observed in the silt fence along the eastern boundaries of the Site, due to staples becoming dislodged from wooden stakes. The straw wattles are still intact.
5. Jute Mesh (Steep Slopes)	N/A	N/A N/A	10/2/ 2021	Severe pooling was observed st Discharge 2. Water saturated the straw waddles and has collected between the silt fence.
6. Temporary Seeding	No (As of 9/2/2021)	No	7/22/2021	Hydroseed has been applied to the earthen access road and handapplication of seed was performed within the area beyond the limit of work that was subjected to Discharge 1. Germination was

Inspection Report for North Sturbridge Road Solar Facility NPDES ID No.: MAR10031G

Inspection Date: 02/04/2022

rispection bate: 02/04/2022						
				observed within areas of disturbed soils within the limits of work; however, little to no germination was observed within the disturbed area downgradient of the limit of work. Additional seed should be hand-applied in this area.		
			10/05/ 2021	The areas downgradient of Discharges 1 and 2 have been stabilized with straw and seed. These areas will be monitored for germination and stabilization.		
7. Topsoil Re-Use	N/A	N/A				
8. Storm Drain Inlets	N/A	N/A		Seedling growth is observed.		
(North Brookfield Road)	N/A	N/A	10/29/ 2021	Localized pooling is observed in the eastern portion		
9. Temporary Drainage Swales	S	14/71		of the site.		
(Throughout Site)	N1/A	N1/0	12/27/	Silt waddle are distributed by		
(moagnout site)	N/A	N/A	2021	growing vegetation in east-		
10. Tomporany Sodimont Pasins	10. Tomporany Sodiment Racins  Ern portion of the site.  Condition and Effectiveness of Pollution Prevention (P2) Practices (CGP Part 2.3)					
Type/Location of P2 Practices [insert additional rows if applicable]	Maintenance Needed?*	Corrective Action Required?*	Date on Which Maintenance or Corrective Action	Notes		
Equipment Refueling	□Yes ⊠No	□Yes ⊠No	First Identified?  [Enter date]			
Staging Area  2. Hydraulic Lines	□Yes ⊠No	□Yes ⊠No	[Enter date]			
Staging/Work Areas	□Yes ⊠No	□Yes ⊠No	[Enter date]			
Equipment Maintenance     Staging Area	□Yes ⊠No	□Yes ⊠No	[Enter date]			
4. Sanitary Toilets	□Yes ⊠No	□Yes ⊠No	[Enter date]			
Staging Area						
5. Vehicle Accident	□Yes ⊠No	□Yes ⊠No	[Enter date]			
Entire Site	□Yes ⊠No	. □Yes ⊠No	[Enter date]			

Inspection Report for North Sturbridge Road Solar Facility

NPDES ID No.: MAR10031G Inspection Date: 02/04/2022

Staging/Work Areas				
8. Concrete Washout	□Yes⊠No	□Yes⊠No	[Enter date]	

Stabilization of Exposed Soil (CGP Part 2.2.14)						
Stabilization Area [insert additional rows if applicable]	Stabilization Method	Have You Initiated Stabilization?	Notes			
Earthen access road leading to stockpile area	Straw mulch or hydroseed	⊠Yes 7/30/2021 □No	The stockpile area and associated access road have been hydroseeded. Germination has begun and the area will be monitored for successful establishment.			
Informal access road along northern portion of the Site	Straw mulch or hydroseed	□Yes [Enter date] ⊠No	Erosion channels are beginning to form within upgradient portions of the informal access road (Figure 1). The contractor indicated that stabilization by smoothing out soils and seeding or spreading mulch would occur on 7/30/2021. Stabilization of this area has not been initiated. After inspection of the area on 8/24/2021, it was determined that			

<sup>\*</sup> Note: The permit differentiates between conditions requiring routine maintenance, and those requiring corrective action. The permit requires maintenance in order to keep controls in effective operating condition. Corrective actions are triggered only for specific conditions, which include: 1) A stormwater control needs repair or replacement (beyond routine maintenance) if it is not operating as intended; 2) A stormwater control necessary to comply with the permit was never installed or was installed incorrectly; 3) You become aware that the stormwater controls you have installed and are maintaining are not effective enough for the discharge to meet applicable water quality standards or applicable requirements in Part 3.1; 4) One of the prohibited discharges in Part 1.3 is occurring or has occurred; or 5) EPA requires corrective actions as a result of a permit violation found during an inspection carried out under Part 4.8. If a condition on your site requires a corrective action, you must also fill out a corrective action form found at <a href="https://www.epa.gov/npdes/stormwater-discharges-construction-activities#resources">https://www.epa.gov/npdes/stormwater-discharges-construction-activities#resources</a>. See Part 5 of the permit for more information.

Inspection Report for North Sturbridge Road Solar Facility NPDES ID No.: MAR10031G Inspection Date: 02/04/2022

			temporary swales would likely alleviate the issue of channelization in this area; however, these swales will not be constructed until work resumes at the Site in October (pending local approval). This area will continue to be monitored; however, stabilization is not required since the area is not discharging sediment beyond the limits of work.
Area beyond the limits of work at Discharge 1	Hand application of seed	⊠Yes 8/24/2021 □No	The sediment deposit previously observed has been removed from beyond the limits of work and the area has been seeded. No sediment migrated within 50 feet of a "water of the US". Straw and additional seed was applied on 8/24/2021 and will be monitored for successful establishment.
Area beyond limits of work at     Discharge 2	Hand application of seed	☐Yes Enter Date ☒No	Stabilization required

Description of Discharges (CGP Part 4.6.6)				
Was a stormwater discharge or other discharge occurring from any part of your site at the time of the inspection?   Yes  No  If "yes", provide the following information for each point of discharge:				
Discharge Location	Observations			
Discharge 1	Describe the discharge: Breach in silt fence allowed runoff to bypass erosion controls.  At points of discharge and the channels and banks of surface waters in the immediate vicinity, are there any visible signs of erosion and/or sediment accumulation that can be attributed to your discharge?   Yes  No  If yes, describe what you see, specify the location(s) where these conditions were found, and indicate whether modification, maintenance, or corrective action is needed to resolve the issue: Small areas of bare soil observed in area immediately beyond perimeter controls. Repairs to erosion controls and re-seeding of damaged areas is required.			

Inspection Report for North Sturbridge Road Solar Facility

NPDES ID No.: MAR10031G

Inspection Date: 02/04/2022

## Contractor or Subcontractor Signature and Certification

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I have no personal knowledge that the information submitted is other than true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."

Signature of Contractor or Subcontractor:

Date:

Printed Name and Affiliation:

Operator Signature and Certification

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information, the information, the information, the information, the information submitted is to the

"I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I have no personal knowledge that the information submitted is other than true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations."


Signature of Operator or "Duly Authorized Representative":

Date:

Printed Name and Affiliation:

Chanler Florian

02/04/2022

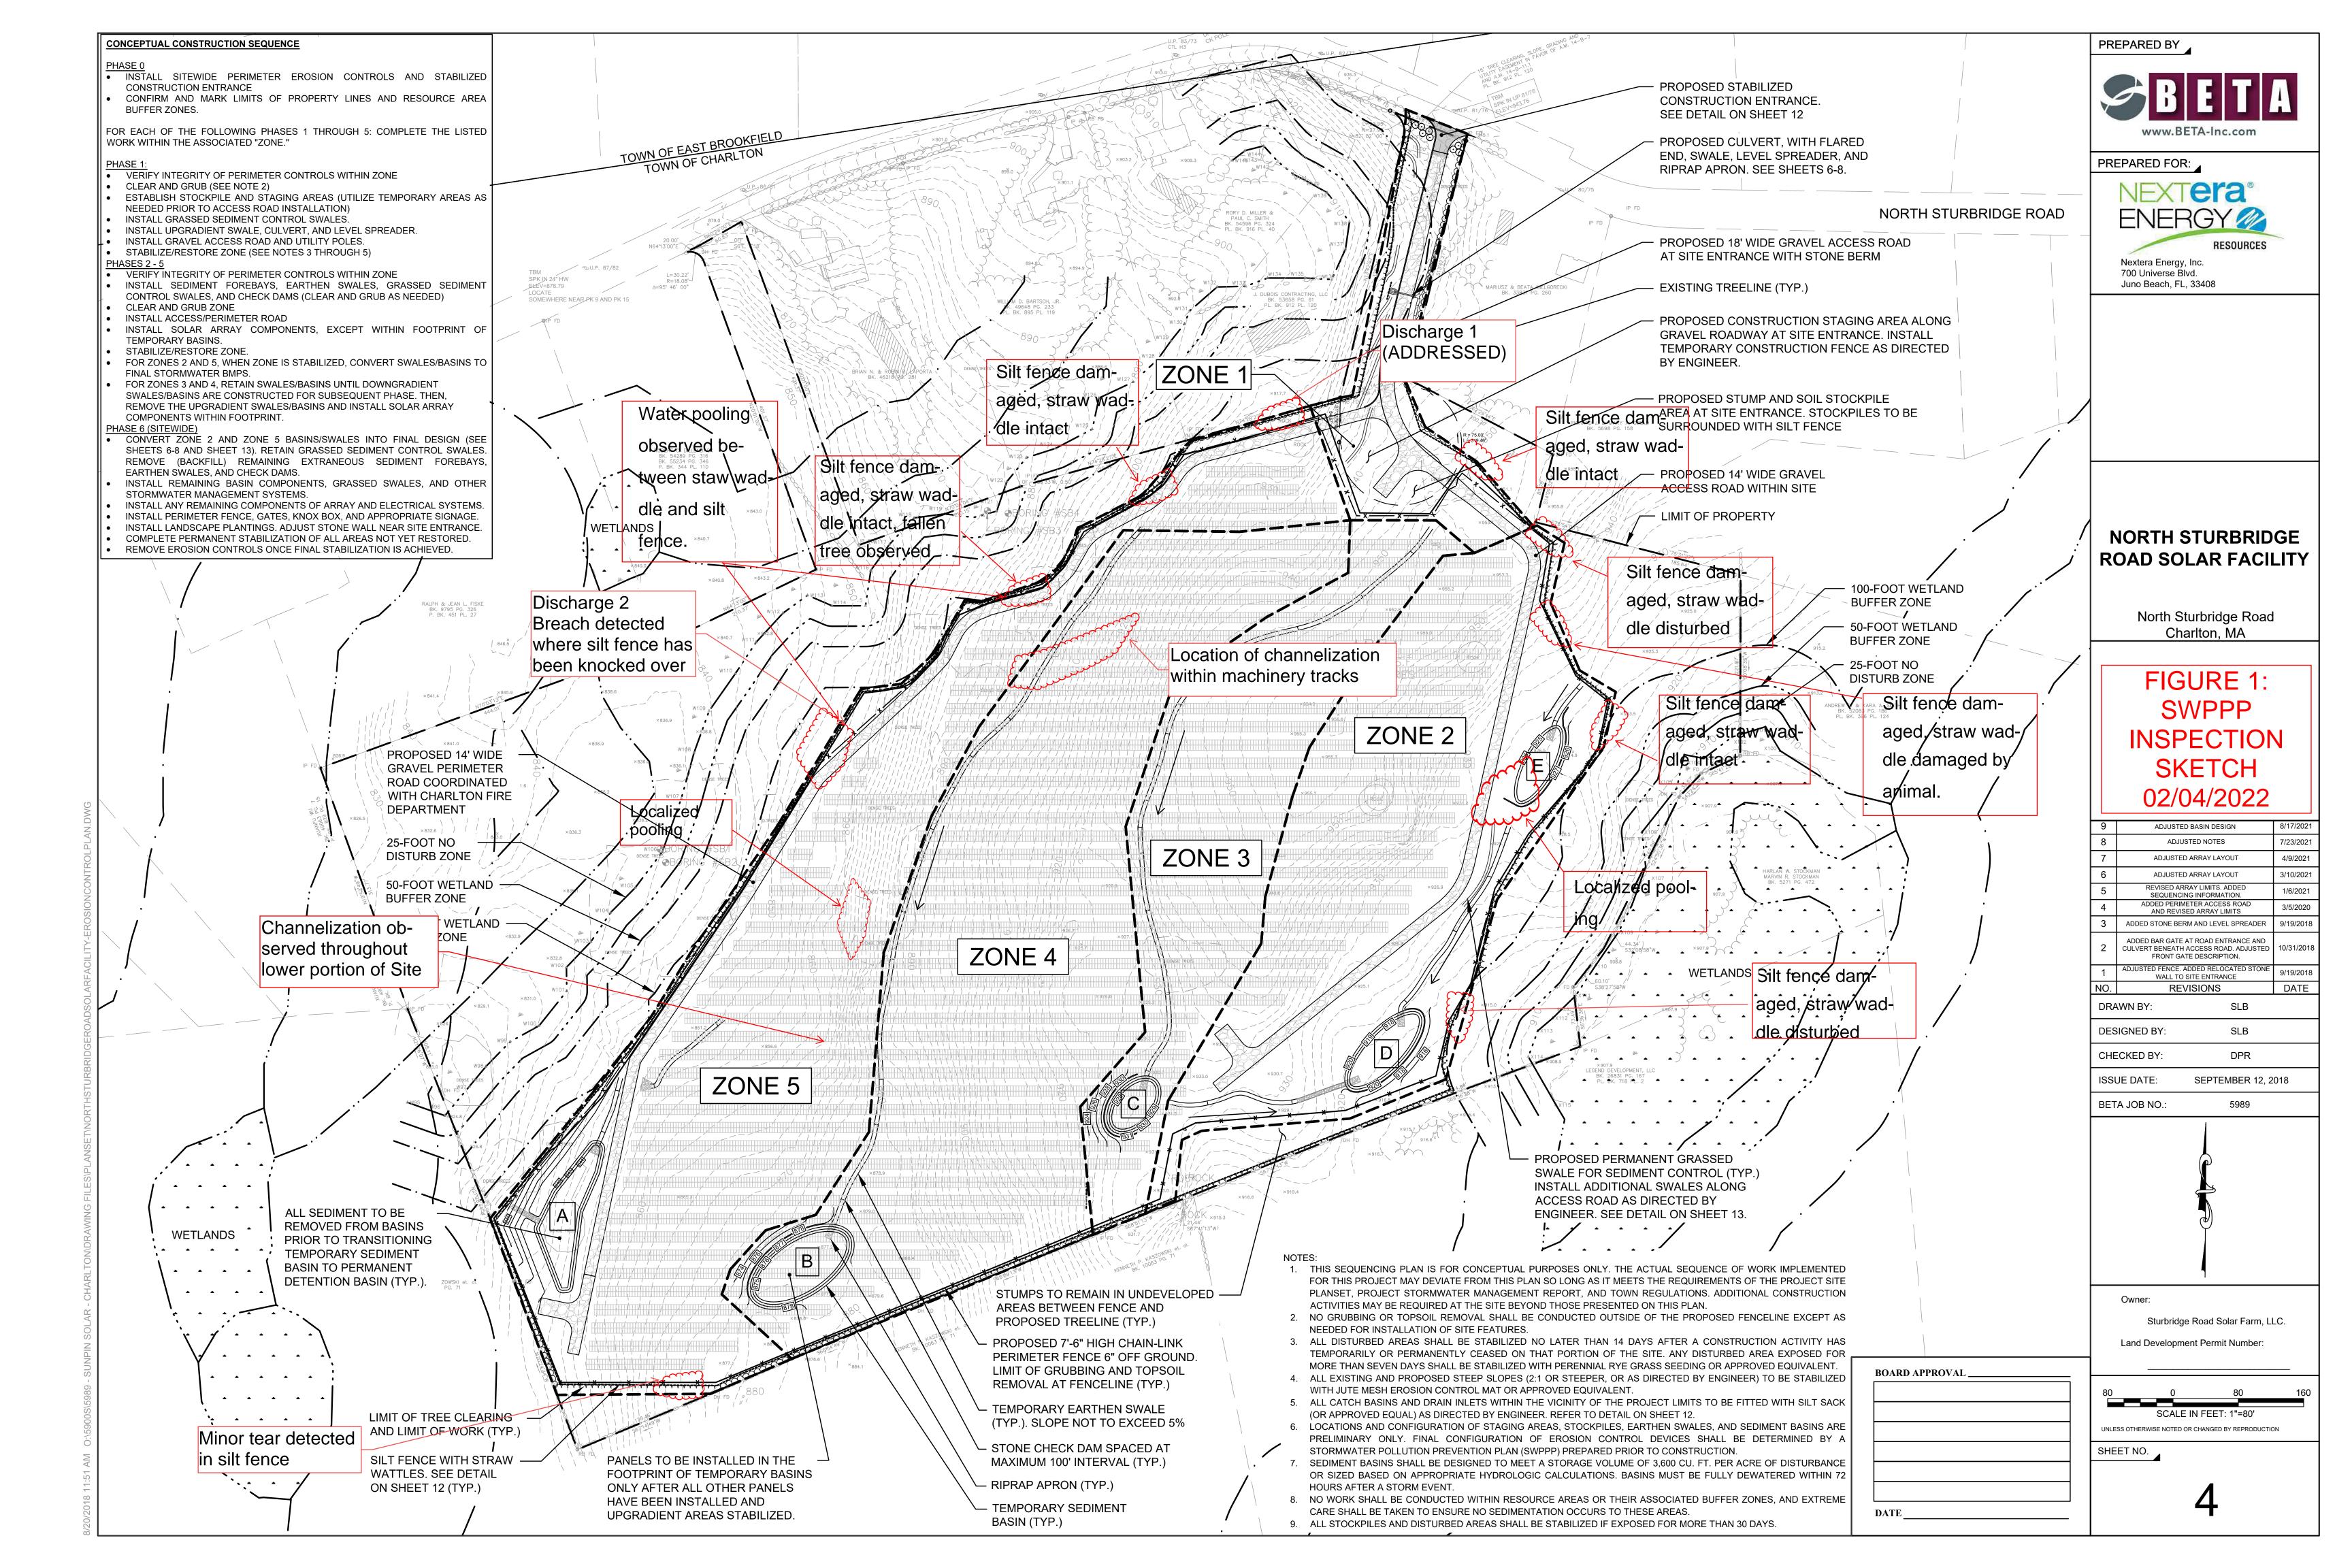

## Photo 1



View of area down-gradient of Discharge 2—facing south west.

## Photo 2



View of area down-gradient of Discharge 2—facing south west.

PHOTOGRAPHIC DOCUMENTATION North Sturbridge Road Solar Facility Charlton, Massachusetts Photographs Documented 02.04.2022

## Photo 3



Photo 4 View of the flooded straw waddle and silt fence located up-gradient from Discharge 2 — Facing north west



View of the flooded straw waddle and silt fence located up-gradient from Discharge 2 — Facing north west

PHOTOGRAPHIC DOCUMENTATION North Sturbridge Road Solar Facility Charlton, Massachusetts Photographs Documented 02.04.2022
